

Release Readiness — GO / NO-GO

Northwind Financial · Global Quality Engineering

GO WITH RISK

READINESS SCORE

+6 vs 24.1

87 /100

Weighted gate composite

TEST PASS RATE

+0.7 pt

98.4%

4,812 / 4,890 passed

OPEN DEFECTS

-55 in 14d

3 High

0 blocker · 0 critical

REQ. COVERAGE

+3 pt

96%

312 / 325 requirements

SECURITY GATE

Action req.

2 High


0 critical open

RELEASE GATE SCORECARD

8 / 10 met

✓ Test pass rate	98.4% / ≥ 98.0%
✓ Blocker / Critical defects open	0 / = 0
✓ High-severity defects open	3 / ≤ 5
✓ Requirements coverage	96% / ≥ 95%
✓ Regression suite executed	100% / = 100%
✓ Automation pass rate	96.5% / ≥ 95%
✓ Code coverage (changed code)	84% / ≥ 80%
✓ Performance budget (p95)	1.82s / ≤ 2.0s
! Security — High vulns open	2 / = 0
! Accessibility (WCAG AA)	1 open / = 0

DEFECT BURNDOWN — 14 DAY COUNTDOWN

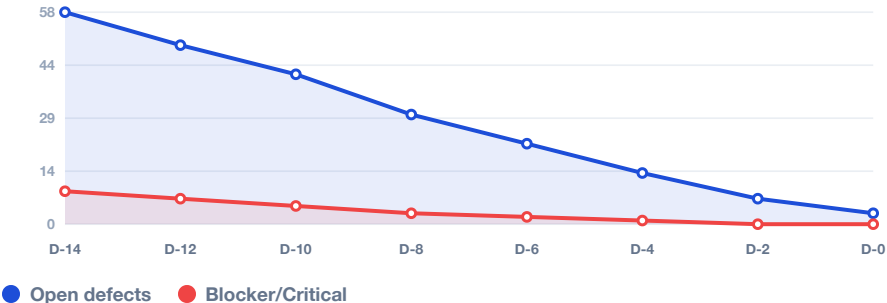

STAKEHOLDER SIGN-OFF

Quality Engineering	Signed
Product Management	Signed
Site Reliability (SRE)	Signed
Security / AppSec	Conditional
Data / Privacy	Signed
Release Management	Pending

OPEN RISKS & MITIGATIONS

ID	RISK	SEV	MITIGATION
SEC-2291	Auth token rotation — 2 high CVEs in 3rd-party lib	High	Patch in 24.2.1 hotfix; WAF rule deployed as compensating control
A11Y-118	Statement export modal fails AA contrast	Medium	Fix scheduled D+3; <2% of users on path
PERF-77	Batch posting p99 spike under peak load	Low	Within budget at p95; capacity headroom verified

RECOMMENDATION

CONDITIONAL GO

Proceed to Wave 1 production with two conditions: (1) deploy 24.2.1 security hotfix within 72h to close SEC-2291; (2) WAF compensating control active at cutover. All functional, regression, performance and reliability gates are met. Blast radius limited to NA/EU; instant rollback verified (4 min).

Quality Trend Report

Northwind Financial · Global Quality Engineering

IMPROVING

DEFECT REMOVAL EFFICIENCY

+8 pt

94%

caught before production

DEFECT DENSITY

-52%

1.4/KLOC

down from 2.9

ESCAPED DEFECTS

-82%

2

this sprint vs 11

DEFECT REOPEN RATE

-2.4 pt

3.1%

first-time-fix 96.9%

MEAN TIME TO FIX


-0.8d

1.9d

critical: 6.4h


DEFECT REMOVAL EFFICIENCY

higher = better

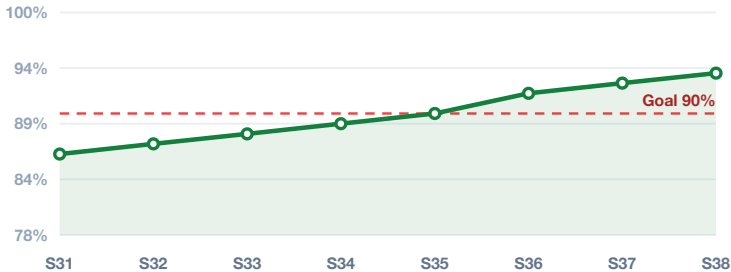


DEFECT DENSITY (PER KLOC)

lower = better

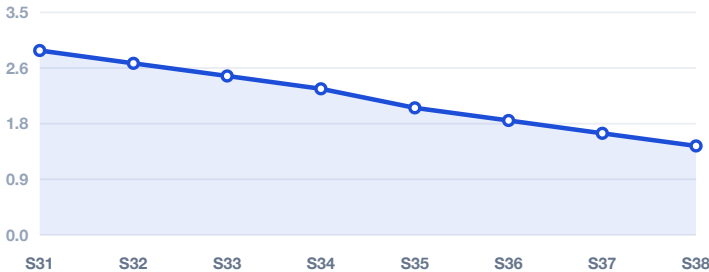


ESCAPED DEFECTS TO PRODUCTION


lower = better

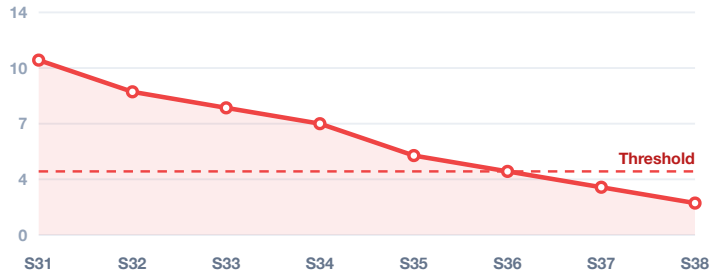

DEFECT INFLOW BY SEVERITY

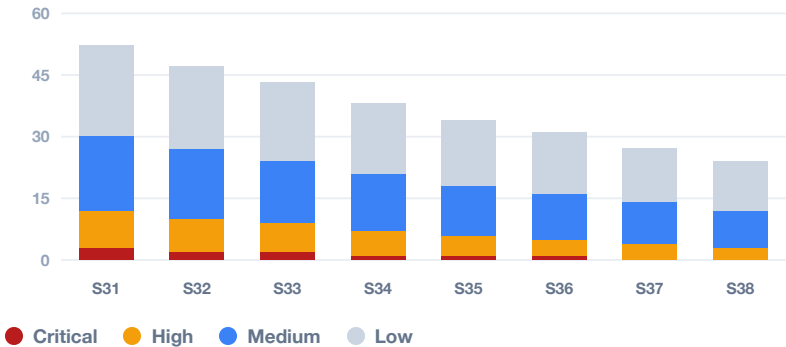

TEST PASS RATE TREND

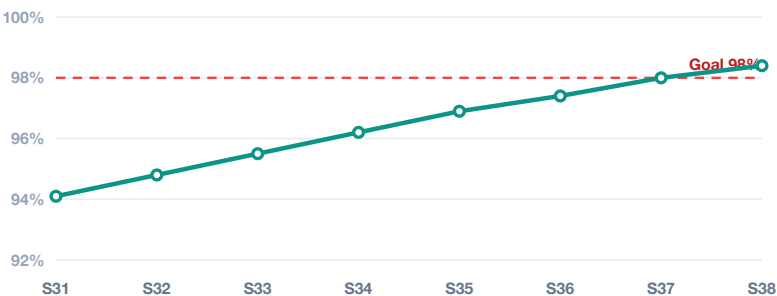

TREND NARRATIVE

- DRE crossed the 90% goal in S36 and holds at 94% — quality is shifting left.
- Escaped defects down 82% over 8 sprints; 6 consecutive sprints under threshold.
- Severity mix flattening — zero criticals injected for two sprints.
- Medium-severity backlog still the largest bucket; targeted for S39 cleanup.

AUTOMATION COVERAGE

+11 pt

78%

3,814 automated tests

SUITE STABILITY

+2.6 pt

96.5%

non-flaky pass rate

FLAKY TESTS

-68%

23

0.6% of suite · was 71

EXECUTION TIME

-44%

19m






4-way parallel (pabot)

CI/CD PASS RATE

+6 pt

98%

last 50 pipeline runs

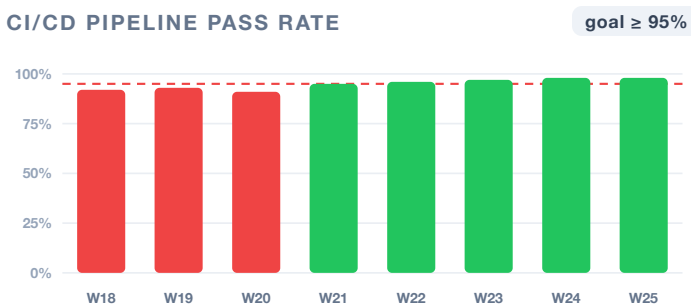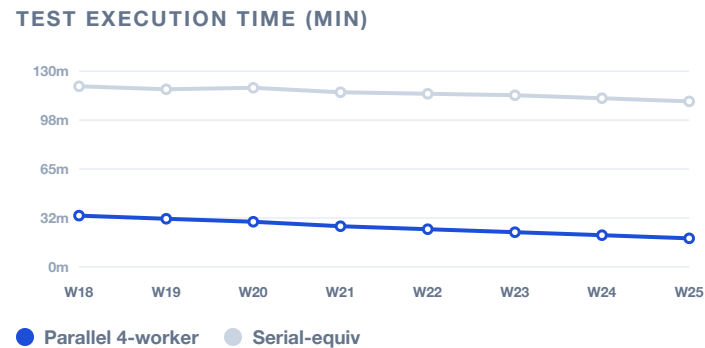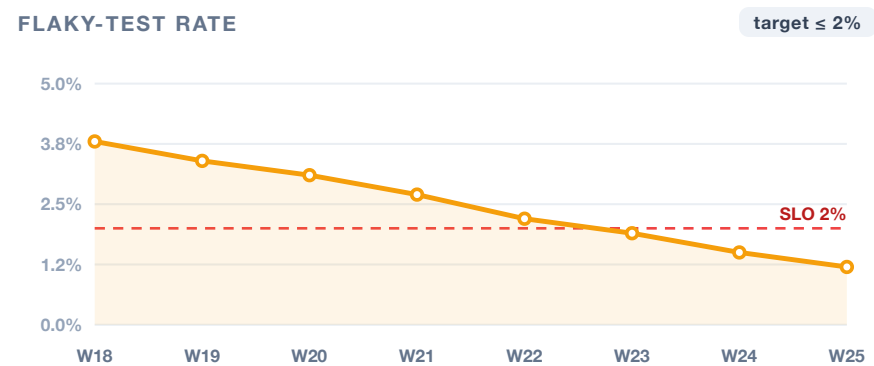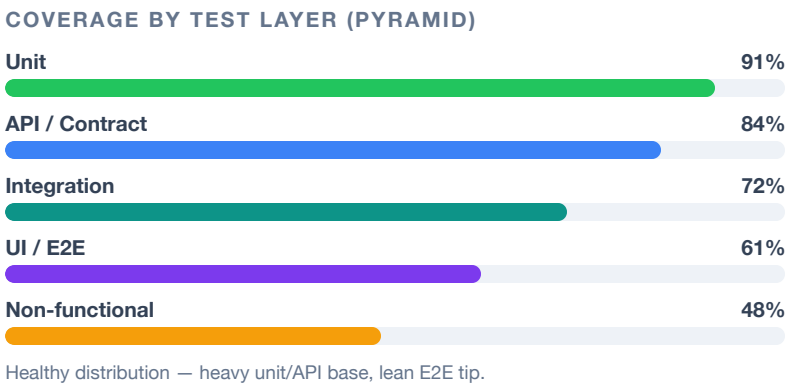

TOP FLAKY TESTS — TRIAGE QUEUE

TEST	FAILS/100	ROOT CAUSE	STATUS
login_mfa_challenge.robot	9	Race on OTP field	Quarantined
statement_export_pdf.robot	6	Async download timing	Fix in review
dashboard_widgets_load.robot	5	3rd-party iframe	Retry+wait added
payments_idempotency.robot	4	Test data collision	Isolated data
search_autocomplete.robot	3	Debounce timing	Stabilized

AVAILABILITY

met 6 mo

99.95%

SLO 99.9% · 21.9m downtime

MTTR

-46%

42m

mean time to restore

MTBF

+5.1d

18.4d

mean time between failures

ERROR BUDGET

on track

38%

remaining this window

INCIDENTS (JUN)

-43%


4

0 Sev1 · 1 Sev2 · 3 Sev3


AVAILABILITY & ERROR BUDGET



MTTR TREND

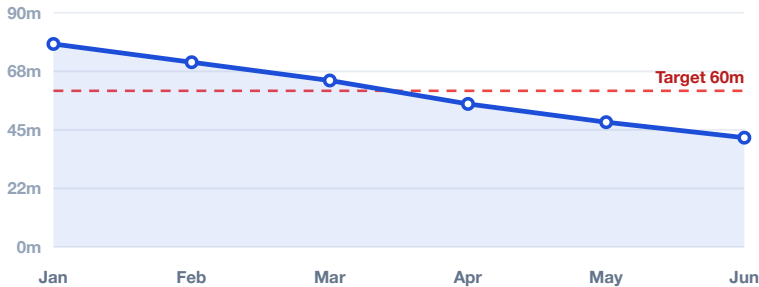

INCIDENT TREND BY SEVERITY

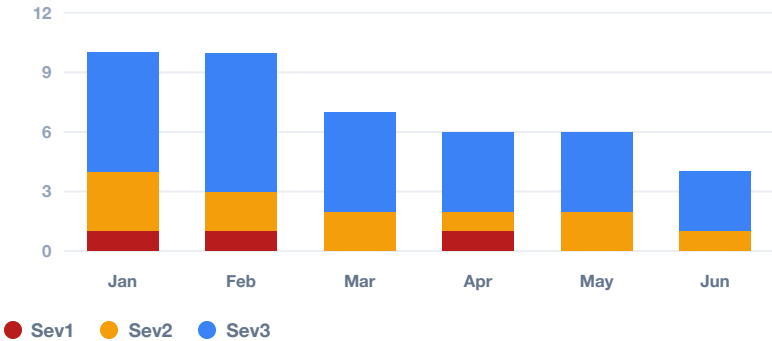

ERROR BUDGET BURN-DOWN (30D)



Burning slower than ideal — budget is healthy; release velocity sustainable.

SLO COMPLIANCE BY SERVICE

availability / SLO / budget left

SERVICE	AVAIL	SLO	BUDGET
Core Banking API	99.98%	99.95%	62%
Payments Service	99.96%	99.95%	44%
Auth / Identity	99.99%	99.99%	18%
Statements	99.93%	99.90%	55%
Notifications	99.91%	99.90%	21%
Web Frontend	99.97%	99.95%	58%
Mobile BFF	99.95%	99.95%	9%

Mobile BFF at 9% budget — flagged for reliability review before next release.

DEPLOYMENT FREQUENCY

4.2 /day

Elite

On-demand, multiple deploys/day



LEAD TIME FOR CHANGES

18 hours

Elite

Commit → production



CHANGE FAILURE RATE

9 %

Elite

Deploys causing degradation



MEAN TIME TO RECOVERY

42 min

Elite


Restore service after failure




DEPLOYMENT FREQUENCY (DEPLOYS/WEEK)



LEAD TIME FOR CHANGES

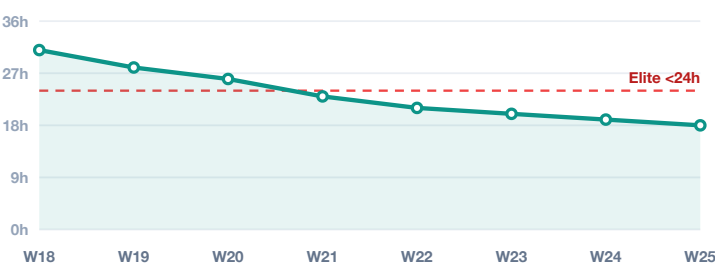

CHANGE FAILURE RATE

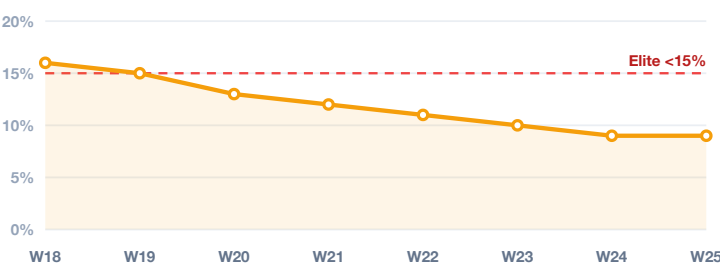

LEAD-TIME VALUE-STREAM BREAKDOWN (18H TOTAL)



Review + deploy-readiness are the largest stages — automation focus for next quarter.

DORA BY SQUAD

SQUAD	DEPLOY FREQ	LEAD TIME	CFR	MTTR	TIER
Payments	5.1/d	14h	7%	31m	Elite
Core Banking	3.8/d	19h	9%	44m	Elite
Identity	4.6/d	16h	8%	38m	Elite
Statements	2.9/d	26h	12%	51m	High
Mobile	3.2/d	22h	11%	47m	High

3 of 5 squads at Elite; Statements & Mobile one tier from Elite — lead-time automation in flight.

● ON TRACK

COMPOSITE QUALITY INDEX

89/100

board target 85 · exceeded

+5 QoQ

AVAILABILITY

99.95%

SLA honored · 0 breaches

6 mo met

CUSTOMER INCIDENTS

4

down from 8 last Q

-40%

AUTOMATION ROI

\$9.6M

annualized cost avoidance

+22%

DELIVERY TIER

Elite

DORA — top 18% industry

↑ tier

COMPOSITE QUALITY INDEX — 4 QUARTER TREND




Blends DRE, availability, escaped-defect rate, automation & DORA into one board-level score.

STRATEGIC QUALITY KPIS — RAG STATUS

● Release Predictability	94%	+9 pt
● Production Availability	99.95%	SLO met
● Customer-Impacting Incidents	4	-40%
● Escaped Defect Rate	0.4/rel	-67%
● Automation Coverage	78%	+11 pt
● Security Posture (High+)	2 open	watch
● DORA Classification	Elite	↑ from High
● Customer Quality NPS	+61	+8

BUSINESS OUTCOME — COST AVOIDANCE (\$M / QUARTER)

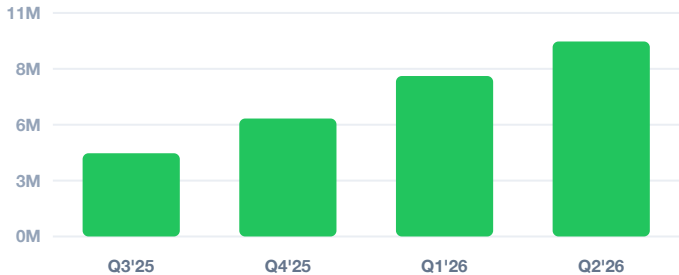

Automation + early defect removal avoided \$9.6M in rework, incident & downtime cost this quarter.

QUARTER WINS

- Achieved **DORA Elite** across the platform — first time in program history.
- Cut customer-impacting incidents **40%**; zero Sev1 in 3 of 6 months.
- Defect Removal Efficiency to **94%**; escaped defects down 82%.
- Release predictability **94%** — 17 of 18 trains shipped on date.

RISKS & WATCH ITEMS

- 2 high-severity security findings open — hotfix train committed for July.
- Mobile BFF error budget at 9% — reliability review scheduled.
- UI/E2E automation at 61% — investment case approved for Q3.

Q3 STRATEGIC FOCUS

- Shift-left security: SAST/DAST gates blocking, target 0 high at release.
- Lift UI/E2E automation 61% → 75%; cut lead-time review stage in half.
- Phase 3 AI: LLM-assisted test generation & flaky-test auto-triage pilot.
- Resilience: chaos-engineering program for top-7 services.
